

LAKEWOOD WEST COLFAX SAFETY PROJECT


WCCA August 16, 2023



PROJECT PROGRESS:

● Phase 1

- Design on track for 100% package
- Median design finalized
 - ❖ Raised Median with planters
 - ❖ Fencing at left turn bays to prevent jaywalking
 - ❖ Fence design used by Maryland DOT

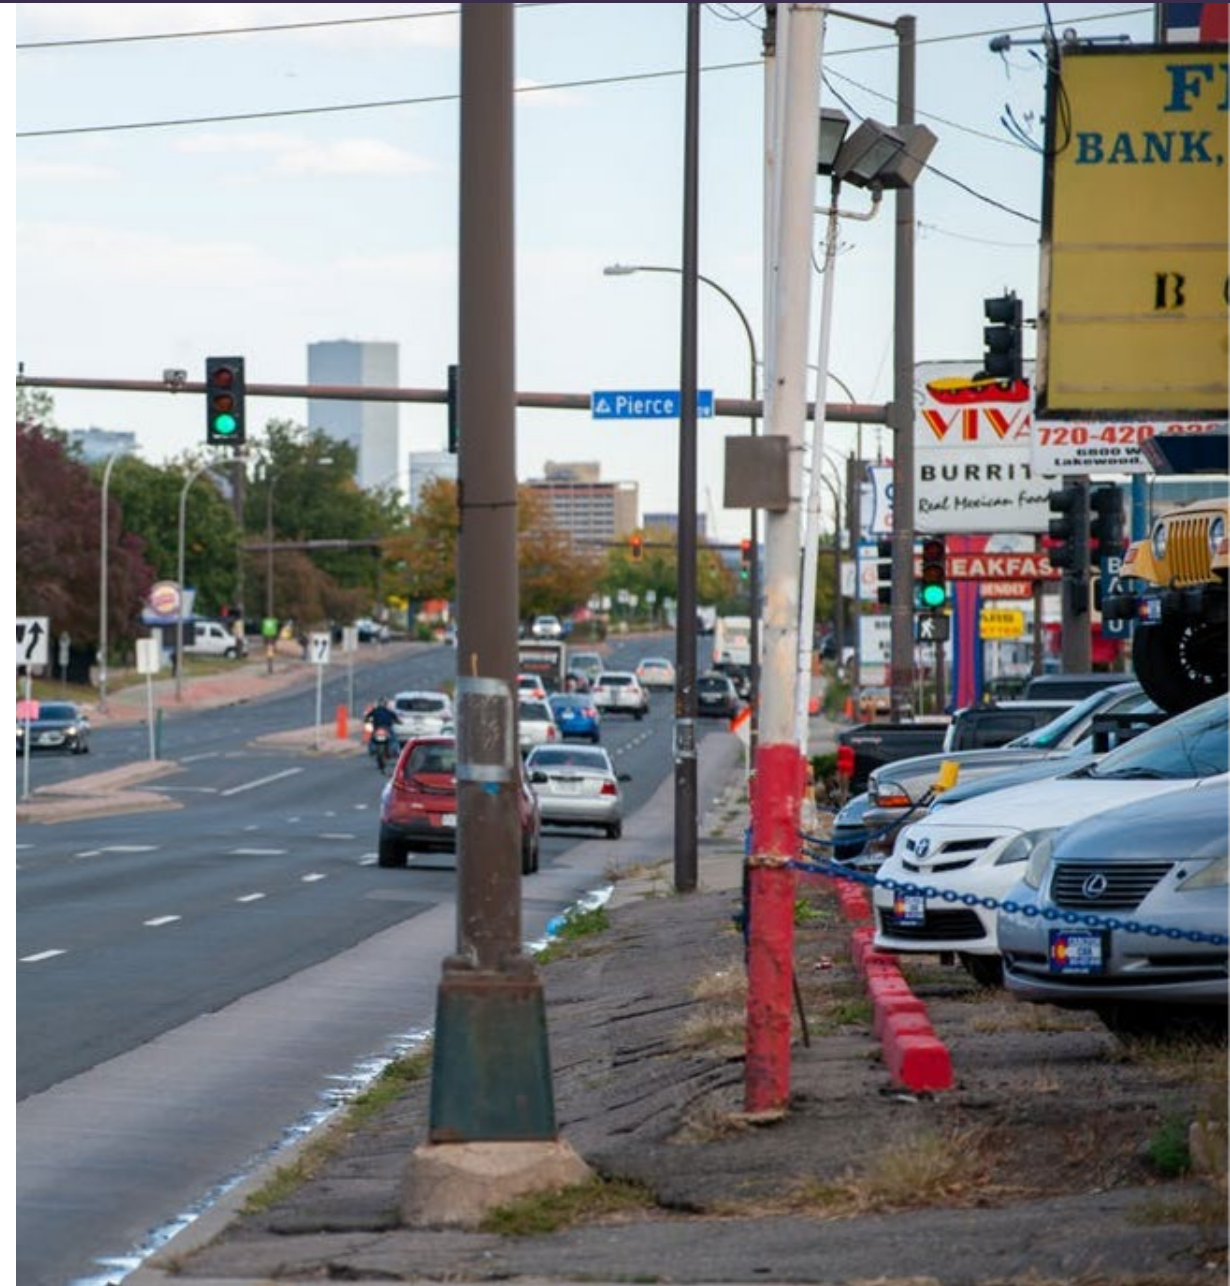


PROJECT PROGRESS:

- **Phase 1**

- Turn bay roadway design complete
- Lighting design underway
- 100% Phase 1 design by end of Fall 2023


- **Utility Coordination Ongoing**

- Consolidated Mutual Water Company
- Xcel Energy
- Additional fire hydrants being designed

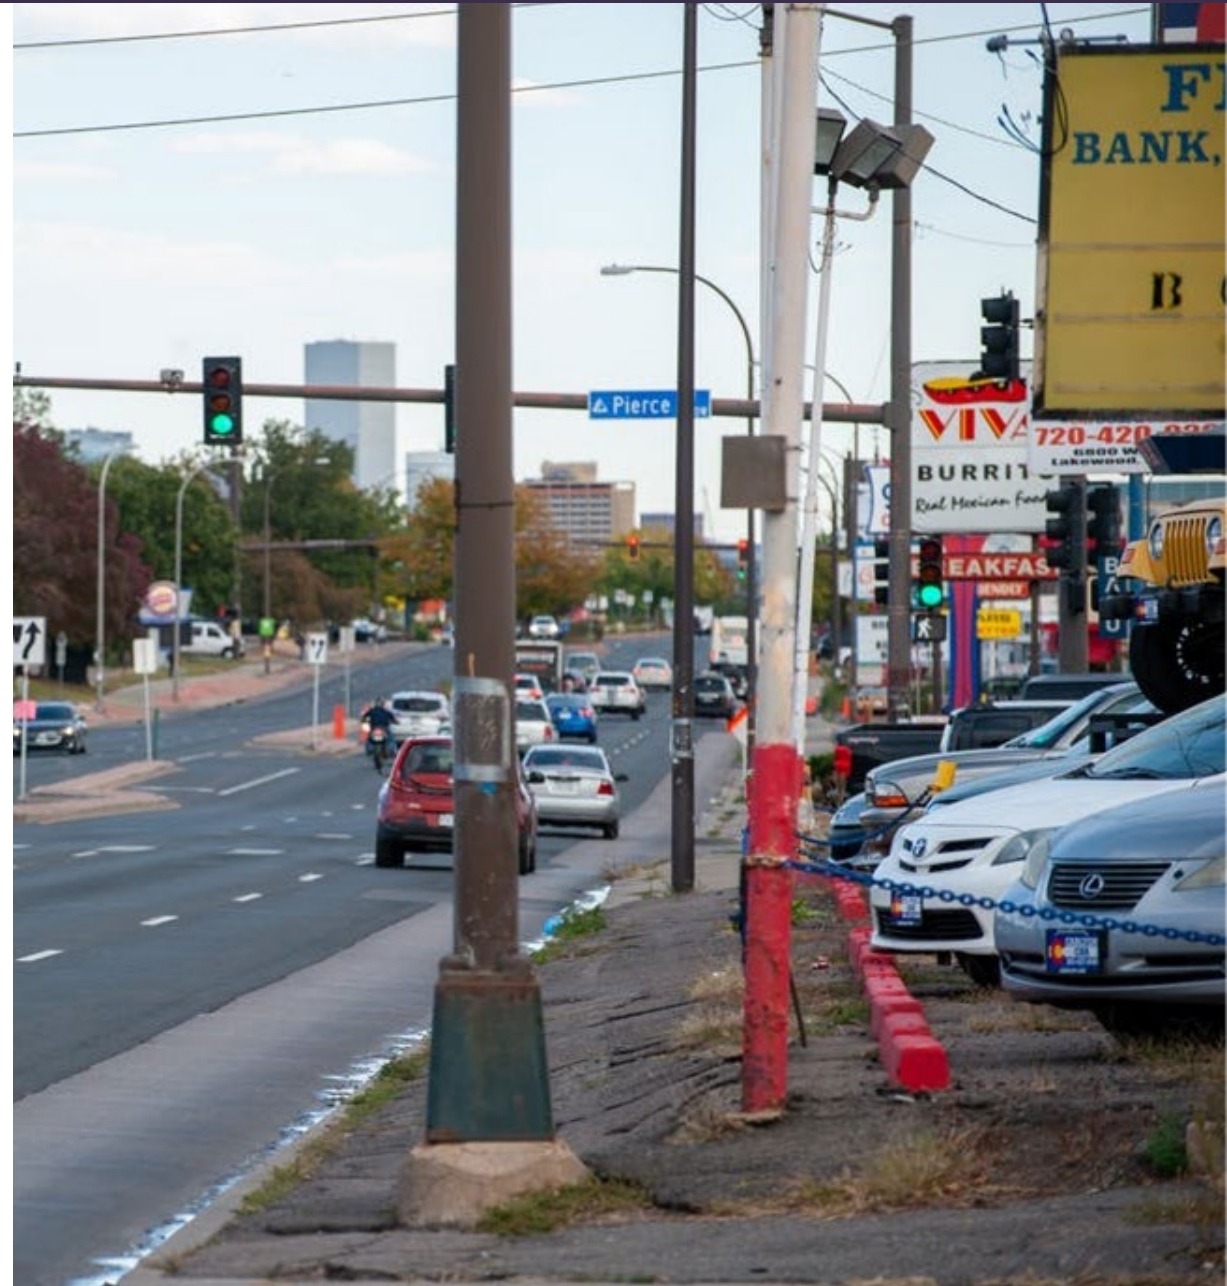


PROJECT PROGRESS:

- **Phase 2 Design Progressing**
- **Utility Coordination Ongoing**
 - **Consolidated Mutual Water Company**
 - **Xcel Energy**
 - **Sanitary sewer and Storm system design**
- **Project Coordination**
 - **North Dry Gulch & W. Colfax Waterline**
 - **West Metro Fire Department**

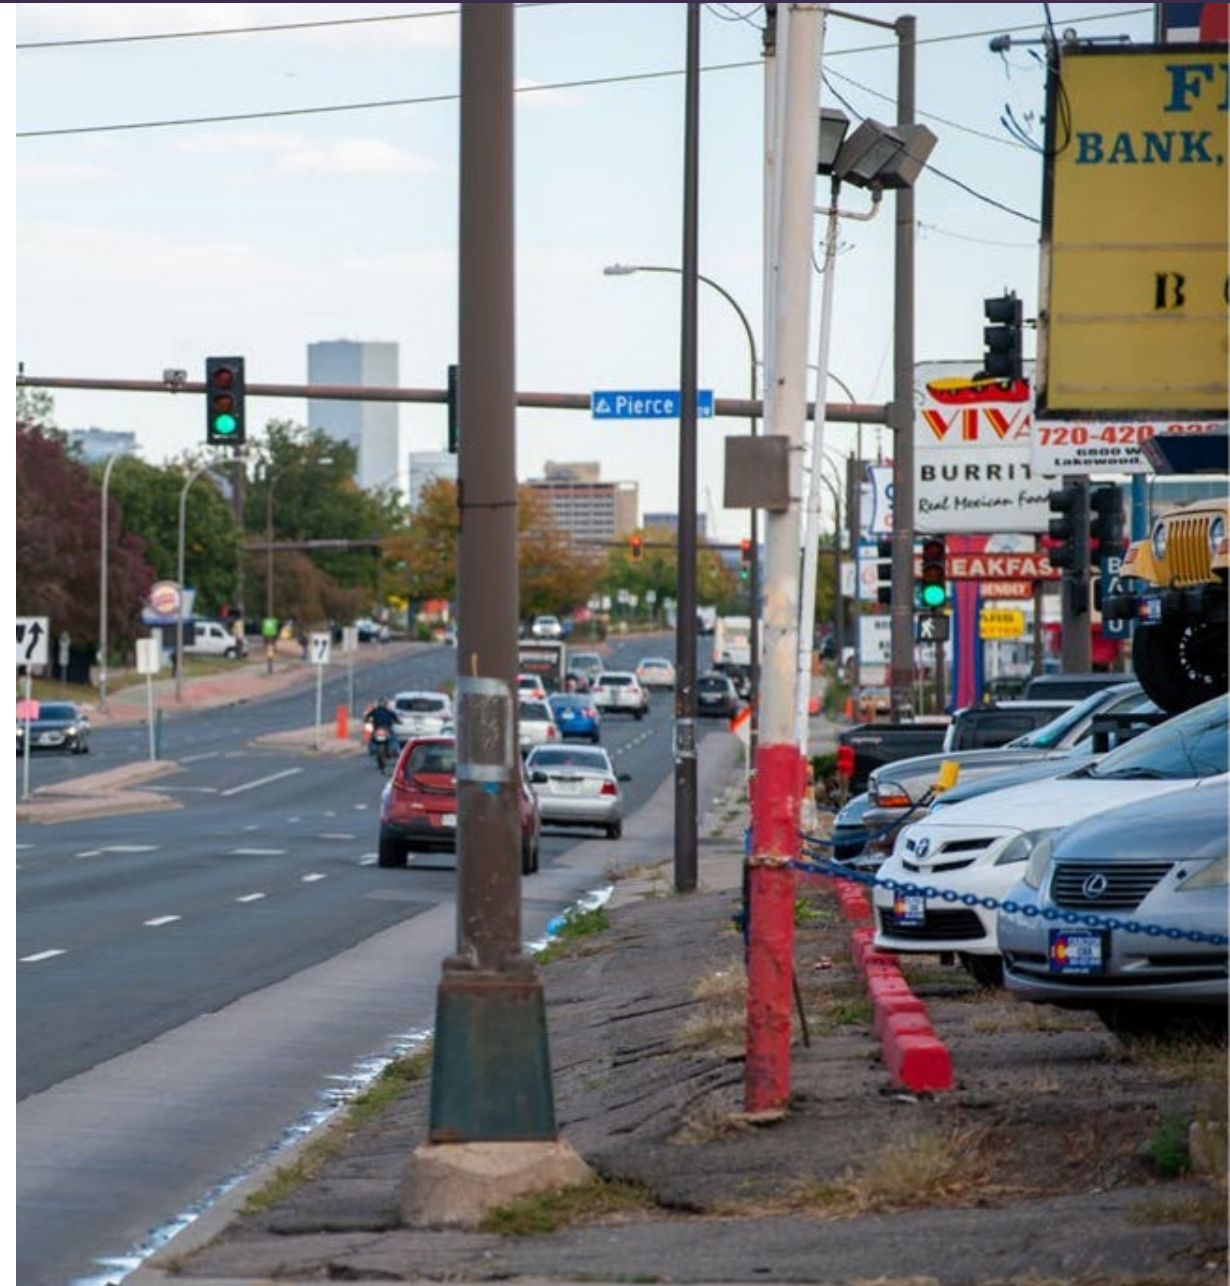

PROJECT PROGRESS:

Proposed Dune Fence at Left Turn Bays

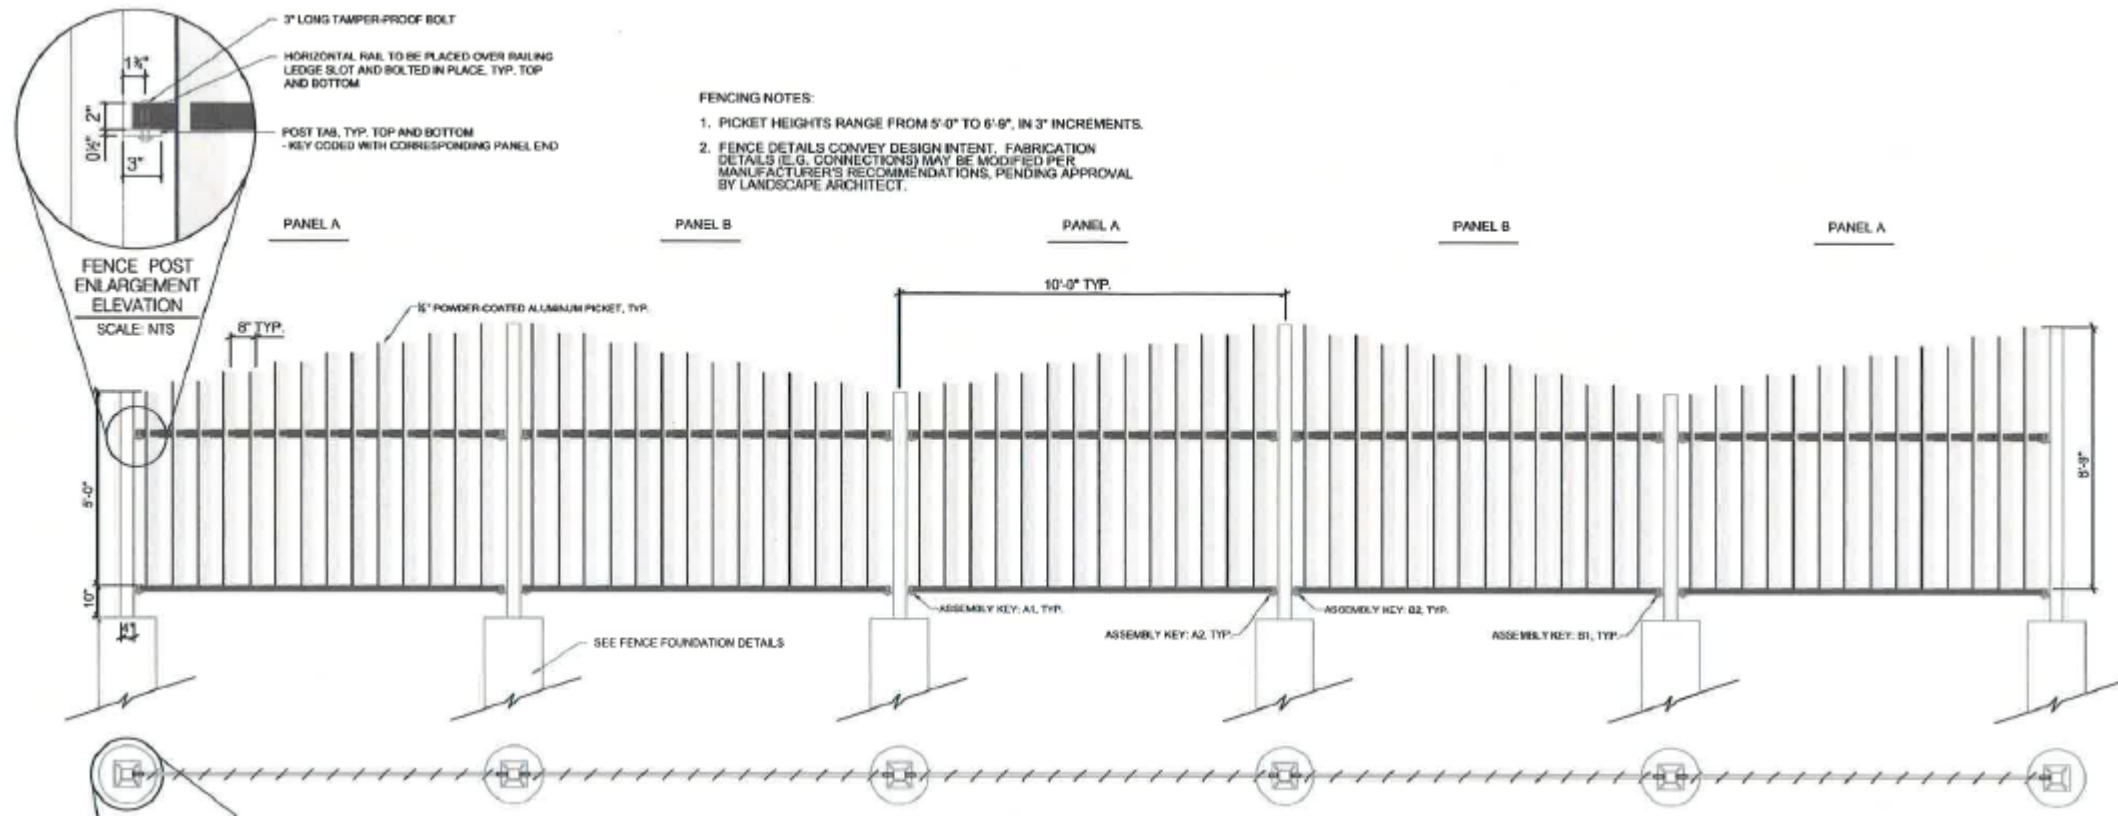


PROJECT PROGRESS:

• Next steps:

- Environmental clearances
- Begin construction for Phase 1 - late Fall 2023
- Continue easement acquisition and clearances for Phase 2
- Ongoing coordination

CONCEPT FRAMEWORK

EDGE: Z-Crossings

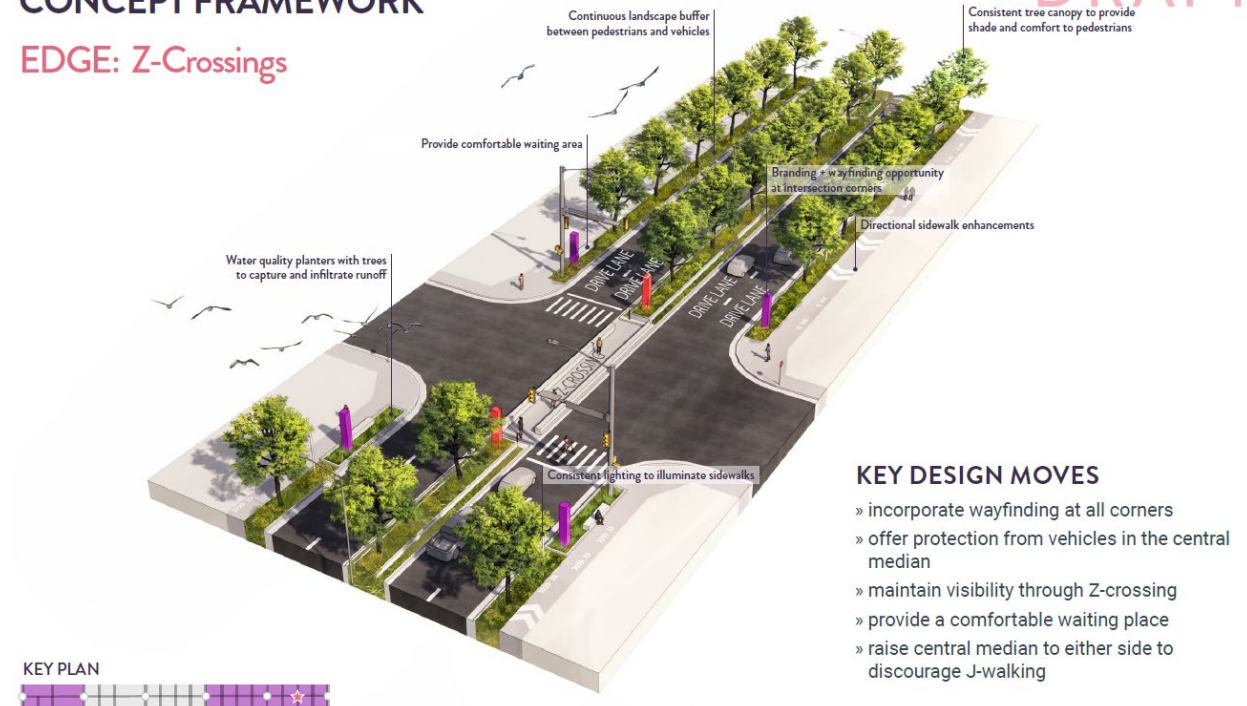

30-DAY COMMUNITY ENGAGEMENT LOOKAHEAD



- Continue to meet with individual business owners as needed
- Community and Stakeholder Engagement Summary Report (posted on website)

Project Website



<https://www.LakewoodTogether.org/WestColfax>

LAKEWOOD

WEST COLFAX SAFETY PROJECT

